

MUNICIPALIDAD DE GENERAL RODRIGUEZ


Obra: "OBRAS VIAL CALLE TARIJA Y 33 ORIENTALES"

Designación: Plan de Trabajo

Descripción	Cantidad	Unidad	TOTAL	Mes 1	Mes 2	Mes 3	Mes 4	Mes 5	Mes 6	Mes 7	Mes 8	Mes 9	Mes 10	Mes 11	Mes 12
Saneamiento de la subrasante	23344,46	M3	\$ 42.348.000,26	\$ 4.234.800,03 10,00%	\$ 4.234.800,03 10,00%	\$ 4.234.800,03 10,00%	\$ 4.234.800,03 10,00%	\$ 4.234.800,03 10,00%	\$ 4.234.800,03 10,00%	\$ 4.234.800,03 10,00%	\$ 4.234.800,03 10,00%	\$ 4.234.800,03 10,00%	\$ 4.234.800,03 10,00%	\$ 0,00 0,00%	\$ 0,00 0,00%
Perfilado y recompactación de sub rasante con cal en 0.20m	38907,44	M2	\$ 27.170.793,77	\$ 2.717.079,38 10,00%	\$ 2.717.079,38 10,00%	\$ 2.717.079,38 10,00%	\$ 2.717.079,38 10,00%	\$ 2.717.079,38 10,00%	\$ 2.717.079,38 10,00%	\$ 2.717.079,38 10,00%	\$ 2.717.079,38 10,00%	\$ 2.717.079,38 10,00%	\$ 2.717.079,38 10,00%	\$ 0,00 0,00%	\$ 0,00 0,00%
Base de hormigon pobre H-17, espesor 0.12m	38907,44	M2	\$ 115.231.508,11	\$ 0,00	\$ 11.523.150,81 10,00%	\$ 11.523.150,81 10,00%	\$ 11.523.150,81 10,00%	\$ 11.523.150,81 10,00%	\$ 11.523.150,81 10,00%	\$ 11.523.150,81 10,00%	\$ 11.523.150,81 10,00%	\$ 11.523.150,81 10,00%	\$ 11.523.150,81 10,00%	\$ 11.523.150,81 10,00%	\$ 0,00 0,00%
Pavimento de H°S° H30 en 18cm de espesor	35370,40	M2	\$ 201.016.081,57	\$ 0,00	\$ 18.091.447,34 9,00%	\$ 18.091.447,34 9,00%	\$ 18.091.447,34 9,00%	\$ 18.091.447,34 9,00%	\$ 18.091.447,34 9,00%	\$ 18.091.447,34 9,00%	\$ 18.091.447,34 9,00%	\$ 18.091.447,34 9,00%	\$ 18.091.447,34 9,00%	\$ 18.091.447,34 9,00%	\$ 20.101.608,16 10,00%
Cordon embutido con estribos y doble hierro	8723,20	ML	\$ 29.911.113,56	\$ 0,00	\$ 2.692.000,22 9,00%	\$ 2.692.000,22 9,00%	\$ 2.692.000,22 9,00%	\$ 2.692.000,22 9,00%	\$ 2.692.000,22 9,00%	\$ 2.692.000,22 9,00%	\$ 2.692.000,22 9,00%	\$ 2.692.000,22 9,00%	\$ 2.692.000,22 9,00%	\$ 2.692.000,22 9,00%	\$ 2.991.111,36 10,00%
Retomado de juntas Pav H°	1135,96	ML	\$ 865.793,16	\$ 0,00	\$ 0,00	\$ 0,00	\$ 86.579,32 10,00%	\$ 86.579,32 10,00%	\$ 86.579,32 10,00%	\$ 86.579,32 10,00%	\$ 103.895,18 12,00%	\$ 103.895,18 12,00%	\$ 103.895,18 12,00%	\$ 103.895,18 12,00%	\$ 103.895,18 12,00%
Limpieza y perfilado de zanja	860,00	ML	\$ 238.668,46	\$ 19.093,48 8,00%	\$ 19.093,48 8,00%	\$ 19.093,48 8,00%	\$ 19.093,48 8,00%	\$ 19.093,48 8,00%	\$ 19.093,48 8,00%	\$ 19.093,48 8,00%	\$ 19.093,48 8,00%	\$ 19.093,48 9,00%	\$ 21.480,16 9,00%	\$ 21.480,16 9,00%	\$ 21.480,16 9,00%
Caños de hormigon armado D=0.60m	300,00	ML	\$ 5.066.986,16	\$ 0,00	\$ 0,00	\$ 0,00	\$ 0,00	\$ 810.717,79 16,00%	\$ 810.717,79 16,00%	\$ 861.387,65 17,00%	\$ 861.387,65 17,00%	\$ 861.387,65 17,00%	\$ 861.387,65 17,00%	\$ 0,00 0,00%	\$ 0,00 0,00%
			\$ 421.848.945,05												

	Mes 0	Mes 1	Mes 2	Mes 3	Mes 4	Mes 5	Mes 6	Mes 7	Mes 8	Mes 9	Mes 10	Mes 11	Mes 12
AVANCE FÍSICO													
AVANCE FÍSICO MENSUAL (\$)	\$ 0,00	\$ 6.970.972,88	\$ 39.277.571,25	\$ 39.277.571,25	\$ 39.364.150,57	\$ 40.174.868,35	\$ 40.174.868,35	\$ 40.225.538,22	\$ 40.242.854,08	\$ 40.245.240,76	\$ 40.245.240,76	\$ 32.431.973,71	\$ 23.218.094,85
AVANCE FÍSICO ACUMULADO (\$)	\$ 0,00	\$ 6.970.972,88	\$ 46.248.544,13	\$ 85.526.115,39	\$ 124.890.265,95	\$ 165.065.134,31	\$ 205.240.002,66	\$ 245.465.540,88	\$ 285.708.394,95	\$ 325.953.635,72	\$ 366.198.876,48	\$ 398.630.850,19	\$ 421.848.945,05
AVANCE FÍSICO MENSUAL (%)	0%	1,65%	9,31%	9,31%	9,33%	9,52%	9,52%	9,54%	9,54%	9,54%	9,54%	7,69%	5,50%
AVANCE FÍSICO ACUMULADO (%)	0%	1,65%	10,96%	20,27%	29,61%	39,13%	48,65%	58,19%	67,73%	77,27%	86,81%	94,50%	100,00%

Curva de Ejecución Física vs Desembolsos

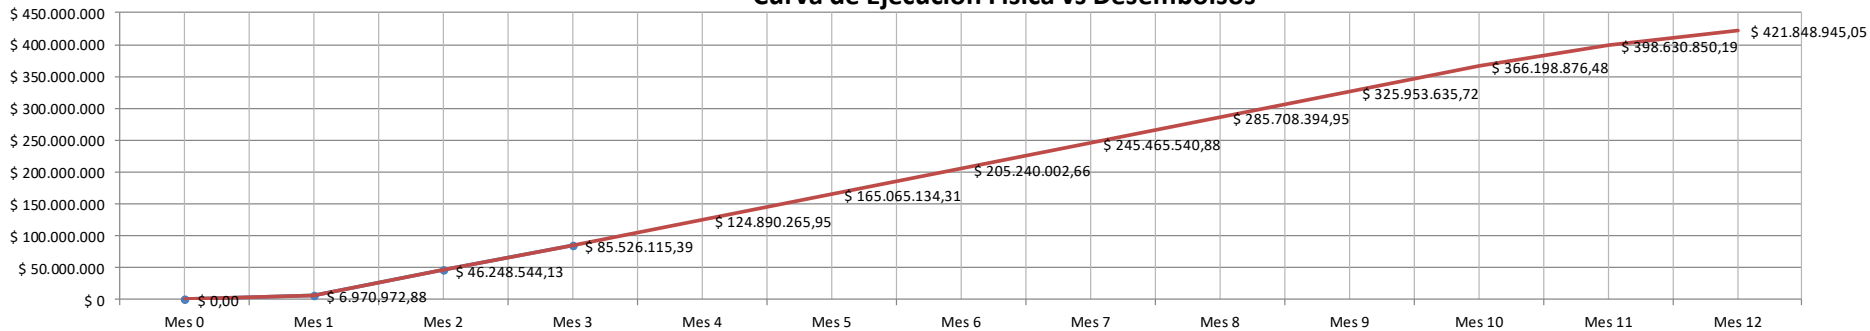

DISTRITO

GRAL.  
RODRIGUEZMINISTERIO DE INFRAESTRUCTURA  
Y SERVICIOS PÚBLICOSGOBIERNO DE LA PROVINCIA DE  
**BUENOS AIRES****COMPUTO Y PRESUPUESTO****OBRAS VIAL CALLE TARIJA Y 33 ORIENTALES**

01	SANEAMIENTO, CALZADA Y LIMPIEZA	UNIDAD	CANTIDAD	MATERIAL	MANO DE OBRA	MAQUINARIA	UNITARIO	TOTAL	INCIDENCIA SOBRE EL TOTAL
1.1	Saneamiento de la subrasante	m3	23.344,46	\$ 273,57	\$ 429,61	\$ 365,49	\$ 1.068,67	\$ 24.947.528,34	10,039%
1.2	Perfilado y recompactación de sub rasante con cal en 0.20m	m2	38.907,44	\$ 123,42	\$ 102,85	\$ 185,13	\$ 411,40	\$ 16.006.520,82	6,441%
1.3	Base de hormigon pobre H-17, espesor 0.12m	m2	38.907,44	\$ 998,00	\$ 426,75	\$ 320,00	\$ 1.744,75	\$ 67.883.755,94	27,316%
1.4	Pavimento de H°S° H30 en 18cm de espesor	m2	35.370,40	\$ 1.298,00	\$ 1.080,00	\$ 970,00	\$ 3.348,00	\$ 118.420.099,20	47,651%
1.5	Cordon embutido con estribos y doble hierro	ml	8.723,20	\$ 750,00	\$ 820,00	\$ 450,00	\$ 2.020,00	\$ 17.620.864,00	7,090%
1.6	Retomado de juntas Pav H°	ml	1.135,96	\$ 175,00	\$ 144,00	\$ 130,00	\$ 449,00	\$ 510.045,32	0,205%
1.7	Limpieza y perfilado de zanja	ml	860,00	\$ 0,00	\$ 124,49	\$ 39,00	\$ 163,49	\$ 140.601,40	0,057%
1.8	Caños de hormigon armado D=0.60m	ml	300,00	\$ 7.000,00	\$ 2.000,00	\$ 950,00	\$ 9.950,00	\$ 2.985.000,00	1,201%
	<b>Subtotal ítem</b>			\$ 10.617,99	\$ 5.127,70	\$ 3.409,62		\$ 248.514.415,02	100,00%

**COSTO - COSTO**

\$ 248.514.415,02

**COSTO NETO**

\$ 37.277.162,25

**A****Gastos Generales**

15,00%

Incidencia sobre (A)

**SUBTOTAL 1**

\$ 285.791.577,27

**B****Gastos Financieros**

4,00%

**Beneficios**

10,00%

Incidencia sobre (B)

**SUBTOTAL 2**

\$ 325.802.398,09

**C****I.V.A e IIBB**

24,50%

Incidencia sobre (C)

**SUBTOTAL 3**

\$ 405.623.985,62

**D****Honorarios Profesionales Representación Técnica**

4,00%

Incidencia sobre (D)

\$ 16.224.959,42

**OBRAS VIAL CALLE TARIJA Y 33 ORIENTALES**

\$ 421.848.945,05
